

Mitch - TPS

From: Denis Zhong - TCS
Sent: Friday, 24 July 2026 5:30 PM
To: Mitch - TCS
Subject: 260724 : ROK Sports Precinct, CIVIL SW V1 Summaries

- 1. Had already exclude thew material regarding to kerb chute as required . (summaries point 4 had already excluded , as kerb chute is not the work scope)
- 2. Due to the pit schedule is not consist with the drawing, I did the take off directly on drawing in GP (items on drawing are more than the pit schedule). Regarding to the pit , the depth of them is really shallow , so allow for 1 base ,one aspro , one cover should be enough for cover the material cost of the pits .
- 3, Hume amended the price , change in spready accordingly.



Regards,

Denis Zhong

TriCore Plumbing Services P/L

TriCore Civil Services P/L

Brisbane • Rockhampton

Brisbane: PO Box 7081, Hemmant QLD 4174

Rockhampton: PO Box 103, Rockhampton QLD 4700

P: 07 3390 5803 | **M:** 0432 471 119

E: denis.z@tricorecivil.com.au

W: tricoreplumbing.com.au | tricorecivil.com.au

From: Denis Zhong - TCS
Sent: Friday, 17 July 2026 12:27 PM
To: Mitch - TCS <mitch@tricorecivil.com.au>
Subject: 260717: ROK Sports Precinct, CIVIL SW V1 Summaries

Hi Mitch ,

Civil SW take off done and transferred into spready, all the quote of main items (rcp , rcbc , trench grate , head wall , hdpe pipe etc) are available .


- 1. Grated trench box and trash box , all prices are available from Reece , and I had put it aside , **exclude in the total material price** , total as 164860.30 put aside in green highlighted .

Grated Trench Drain and Trash box		
GT1. RECYFIX PRO 200 CLASS B 125, TYPE 010 WITH FIBRETEC SLOTTED GRATING	129	m
GT2 RECYFIX PRO 200 CLASS B 125, TYPE 010 WITH FIBRETEC SLOTTED GRATING	144	m
GT3 RECYFIX PRO 200 CLASS B 125, TYPE 010 WITH FIBRETEC SLOTTED GRATING	146	m
GT4 RECYFIX PRO 200 CLASS B 125, TYPE 010 WITH FIBRETEC SLOTTED GRATING	144	m
GT5 RECYFIX PRO 100 CLASS B 125, TYPE 010 WITH STAINLESS STEEL ANTI-SLIP HEELGUARD GRATING	16	m
GT6 RECYFIX PRO 200 CLASS D 400, TYPE 010 WITH HEELGUARD G-TEC DUCTILE IRON GRATING	32	m
GT7 RECYFIX PRO 100 CLASS B 125, TYPE 010 WITH STAINLESS STEEL ANTI-SLIP HEELGUARD GRATING	4	m
GT8 RECYFIX PRO 100 CLASS B 125, TYPE 010 WITH STAINLESS STEEL ANTI-SLIP HEELGUARD GRATING	6	m
GT9 RECYFIX PRO 100 CLASS B 125, TYPE 010 WITH STAINLESS STEEL ANTI-SLIP HEELGUARD GRATING	4	m
end cap fpr 100mm trench grate	10	ea
End cap for 200 mm grate trench	8	ea
HAURATON TRASH BOX 100	4	ea
HAURATON TRASH BOX 200	25	ea
estimate transprot for grate trench and trash box	1	ea
ROCK AND EROSION CONTROL MATTING for kerb chute		

2. 100 mm sub soil drain , measure as 2173 meters on plan , put it aside , **exclude in the total material price.**

8	
9	100mm socked ag pipe
0	100mm socked ag pipe

3. exclude all the swales ,

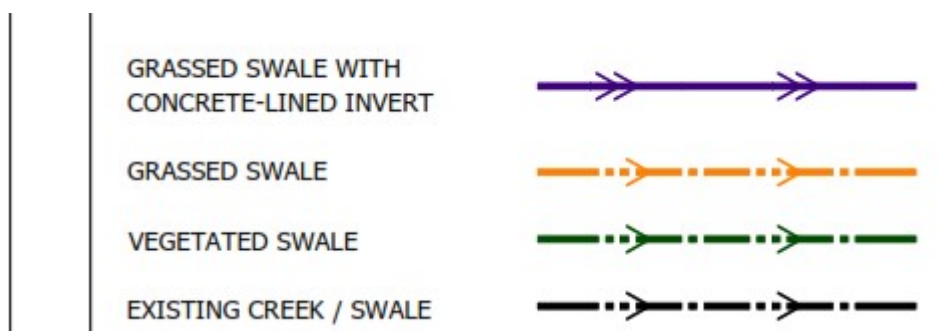


4. for all the kerb chute , only allow for rock and erosion contraol mat, exclude concrete kerb ,

In excel spready

ROCK AND EROSION CONTROL MATTING for kerb chute



ROCK :DIA 100 , 180 thickness (measure area 56m2)
erosion control matting

In ground plan

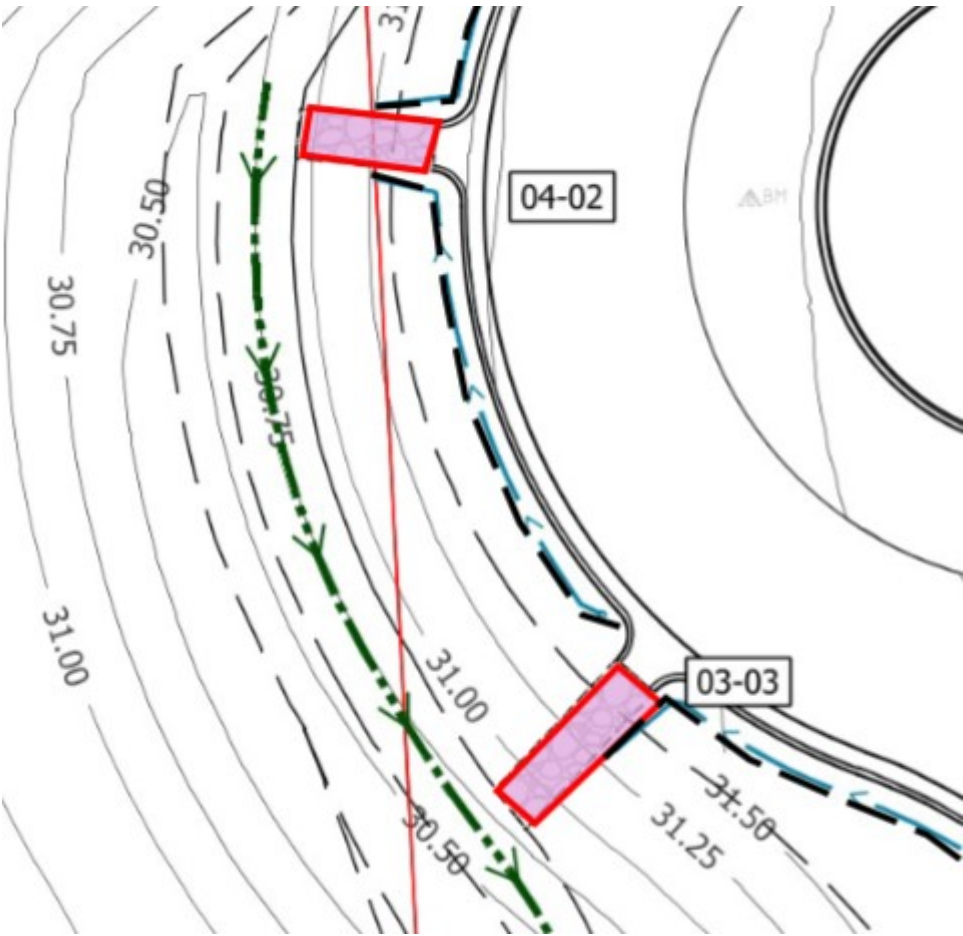

13-02	KERB CHUTE		1.000			
14-02	KERB CHUTE		1.000			
15-02	KERB CHUTE		1.000			
16-02	KERB CHUTE		1.000			
17-02	KERB CHUTE		1.000			
18-02	KERB CHUTE		1.000			

In drawing F1325

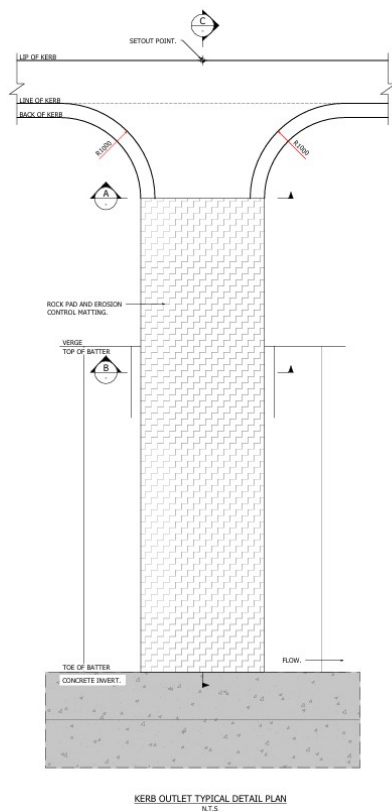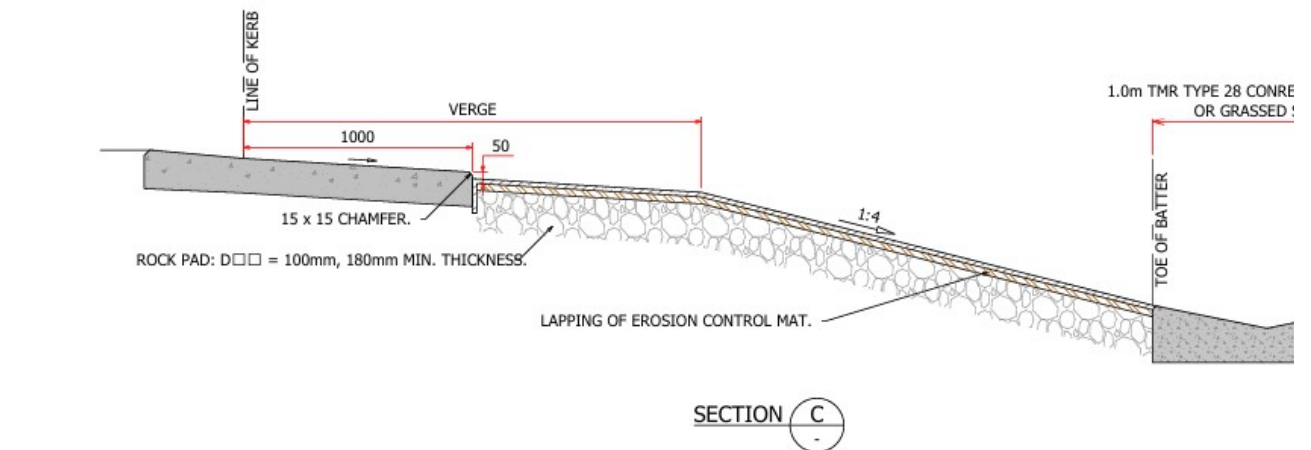

5. for the Excavation/Quarry/Misc/ Takeoff., L/M of Inground Pipe (Average Depth) , total meter is 1883 meters , which include all the rcp pipe . hdpe pipe , pvc pipe , and also drainage culvert , need to put more allow more allowance for excavation and bedding material of the CULVERT ?

Also , I have put the trench drainage and trash box aside , have excluded the excavation and quarry for treanc drainage now , need to put allowance for the excavation and quarry for them if decide to include grate trench and trash box into the quote ?

6. WSUD FILTRATION SYSTEM in the front page , Atlan estimate it due to lack of specific model no,

WSUD FILTRATION SYSTEM	
Cost	\$ 88,838.00
Markup	10%
Charge =	\$ 97,721.80
install estimate	\$ 6,000.00
fuel levy estimate	\$ 2,500.00
	\$ 106,221.80



Regards,

Denis Zhong

TriCore Plumbing Services P/L

TriCore Civil Services P/L

Brisbane • Rockhampton

Brisbane: PO Box 7081, Hemmant QLD 4174

Rockhampton: PO Box 103, Rockhampton QLD 4700

P: 07 3390 5803 | **M:** 0432 471 119

E: denis.z@tricorecivil.com.au

W: tricoreplumbing.com.au | tricorecivil.com.au
